


The Hazel McCallion Line LRT

Construction Liaison Committee Meeting

July 2024



Hazel McCallion LRT

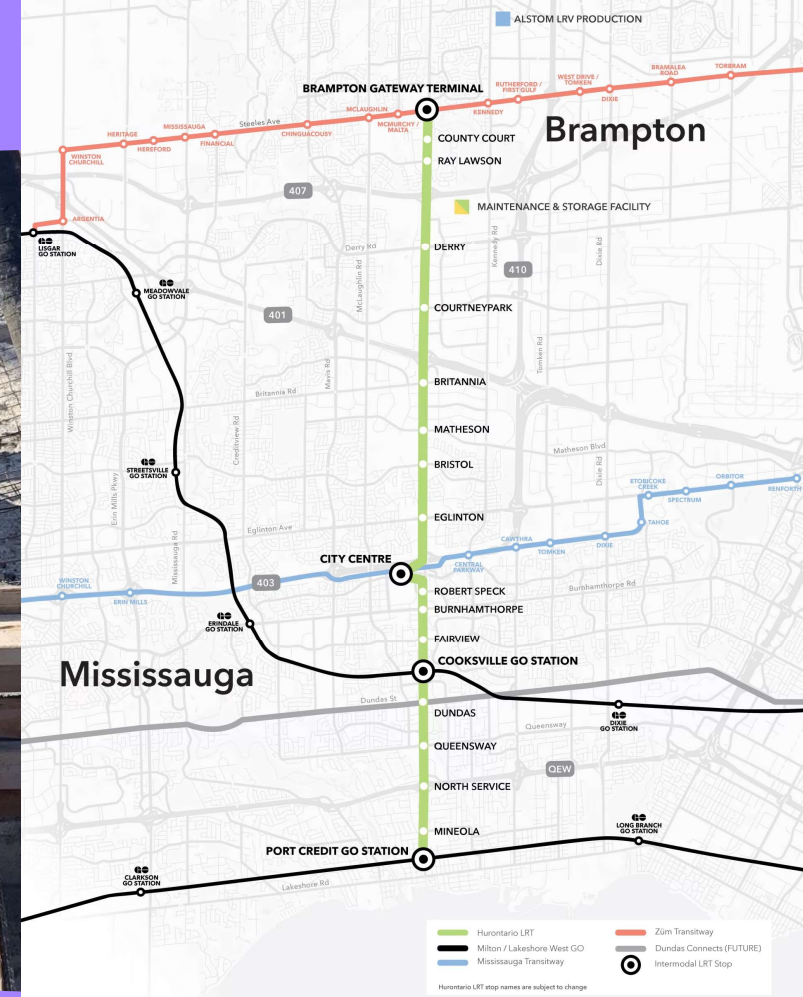

LAND ACKNOWLEDGEMENT

Let us take a moment to acknowledge that we are on the traditional territory of Indigenous Peoples, including the Anishnabeg, the Haudenosaunee and the Wendat peoples.

We are all Treaty people. Many of us have come here as settlers and immigrants—in this generation or generations past.

Metrolinx declares its commitment to building meaningful relationships with Indigenous Peoples. We acknowledge we have a responsibility to recognize and value the rights of Indigenous Peoples and conduct business in a manner that is built on the foundation of trust, respect and collaboration.

We acknowledge the historic and continued impacts of colonialization, the many broken promises and treaties, and the need to work towards reconciliation with the original caretakers of this land... today and for future generations.

SAFETY MOMENT

AGENDA

- **5min:** Welcome & Introductions
- **10min:** Terms of Reference Review
- **15min:** Construction Updates
- **30min:** Discussion



MISSISSAUGA SOUTH

Mississauga South

Completed Works

- New Eaglewood bridge reopened on July 4, 2024
- Inglewood bridge demolished (Week of July 9, 2024)
- All electric work between Park Street and Inglewood has been completed. Handover to utility partner in this area also completed.
- Installation of primary conductors has been completed between Mineola Road and Pinewood

Current Works

- Road widening continues along the west side of Hurontario Street (Expected to be completed by end of July 2024)
- Electrical, plumbing, masonry and other works at Port Credit Station (Summer 2024)
- Hydro pole erections near QEW (Summer 2024)
- Lighting works in the QEW Pushbox (End of July 2024)



Look ahead

- Construction of guideway at Mineola Road intersection (22 July to August 19, 2024 pending city approvals)
- New Alectra connections to adjacent properties (Summer/Fall 2024)
- Removal of old hydroelectric poles (Summer 2024)
- Grading changes to match elevations (Fall 2024)
- Architectural finishes to the Port Credit Station (Fall 2024)
- Platform level plumbing works at Port Credit Station (Scheduled for completion by mid-August)
- Flood walls construction completed at Mary Fix Creek

COOKSVILLE

Current Work

- Road widening between Bronte College and Dundas
- Track installation at The Queensway (August 2024)
- Telecom manhole works at the southwest corner of Hurontario and Dundas (Scheduled for completion end of July 2024)
- Alectra duct bank works from Hillcrest to John Street (Early-August 2024)
- Installation of Traction Power Substation (TPSS) at Central Parkway (Box to be delivered end of July 2024)
- Track installation between Fairview Road and Matthews Gate
- Preparatory works for Fairview Stop (Summer 2024)
- Sanitary and other connections between Dundas and Paisley



Look ahead

- Telecom installation between The Queensway and Fairview Road (Fall 2024)
- Telecom manhole works on east of Dundas and Hurontario (Summer 2024)
- Construction of Fairview Road Stop (End of Summer 2024)
- Installation tracks at Hillcrest, King Street, Paisley Boulevard and Bronte College Court (Summer/Fall 2024)

MISSISSAUGA CENTRE

Current Work

- Track installation at Burnhamthorpe Road from July to September, resulting in temporary lane reductions and turn reductions. Weekend works scheduled from July 27-30 and August TBD
- Telecom infrastructure installation
- Guideway works from Robert Speck to Square One Drive (Summer 2024)
- Robert Speck Parkway Stop construction (Summer 2024)
- Preparatory works for Burnhamthorpe Stop (Summer 2024)
- Switchgear connections from Elia Avenue to Eglinton Avenue (Scheduled for completion by end of July 2024)

Elevated Guideway

- Retaining walls and abutments construction continues for the elevated guideway
- The elevated guideway has now reached halfway over Hwy.403. Piers are being constructed on the north side (Summer/Fall 2024)



Look ahead

- Weekend works for Burnhamthorpe track installation
- Completion of Highway 403 Bridge rehab (end of August 2024)
- TPSS construction completion north of Highway 403(Summer/Fall 2024))
- OCS pole installation between Eglinton and Elia
- Electrical conduit and telecom installations over the elevated guideway (Fall 2024)

MISSISSAUGA NORTH

Current Work

- Installation of Traction Power Substations (TPSS) at Britannia, Longside, Matheson, Elia and Eglinton (Spring/Summer 2024)
- Continued utility relocations and upgrades
- Energization of TPSS along the segment (Fall 2024)




Look ahead

- Installation of Overhead Catenary System (OCS) poles (Summer/Fall 2024)
- Embedded track installations throughout the midblock
- Continued track work leading into the Operations, Maintenance and Storage Facility (OMSF)
- Installation of canopies at some stops (Fall/Winter 2024)
- TPSS (Fall/Winter 2024)

BRAMPTON SOUTH

Current Work

- Partial driveway closures for road widening activities (Summer/Fall 2024)
- Installation of irrigation lines
- Hydrant relocations and new installations (Summer 2024)
- Traffic configuration change at the Highway 407 ETR overpass (Summer 2024)
- Widening of the southeast on-ramp to Highway 407 ETR (Summer 2024)

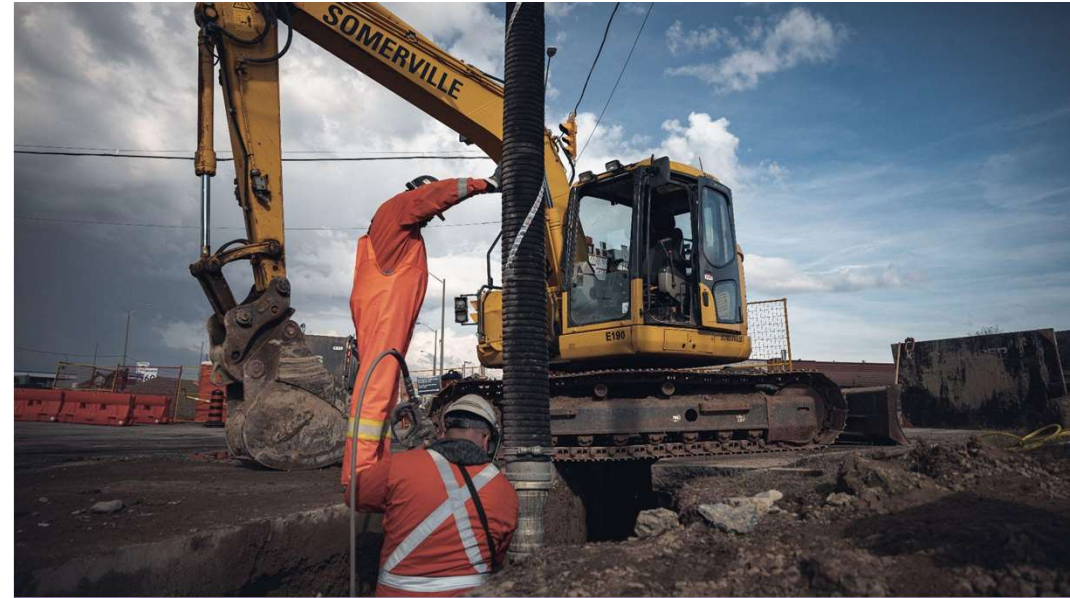

Look ahead

- Continuation of work on new Highway 407 ETR structures
- Installation of stormwater management infrastructure
- Continuation of boulevard runs
- TPSS Construction (Fall/Winter 2024)

IN THE COMMUNITY

CONTACT US

Questions?

Follow us on Instagram, Facebook & X
@HMcCallionLine

Call Us

416-202-7500

Email Us

peel@metrolinx.com

Stay up to date with Metrolinx
projects [Metrolinx.com/peel](https://www.metrolinx.com/peel)

Learn more at [metrolinx.com](https://www.metrolinx.com)!



Metrolinx Peel Community Office:

3024 Hurontario Street Unit G12
Mississauga, ON. L5B 4M4

